


SIGNATURE \_\_\_\_\_  
DATE 02-23-2023

REVISIONS		
NO.	DESCRIPTION	DATE

PROJECT NUMBER 0944401  
DATE OF ISSUE 02-23-2023  
DRAWN BY BA  
CHECKED BY LL

PEDESTRIAN TRAFFIC  
CONTROL PLAN

C200  
BID

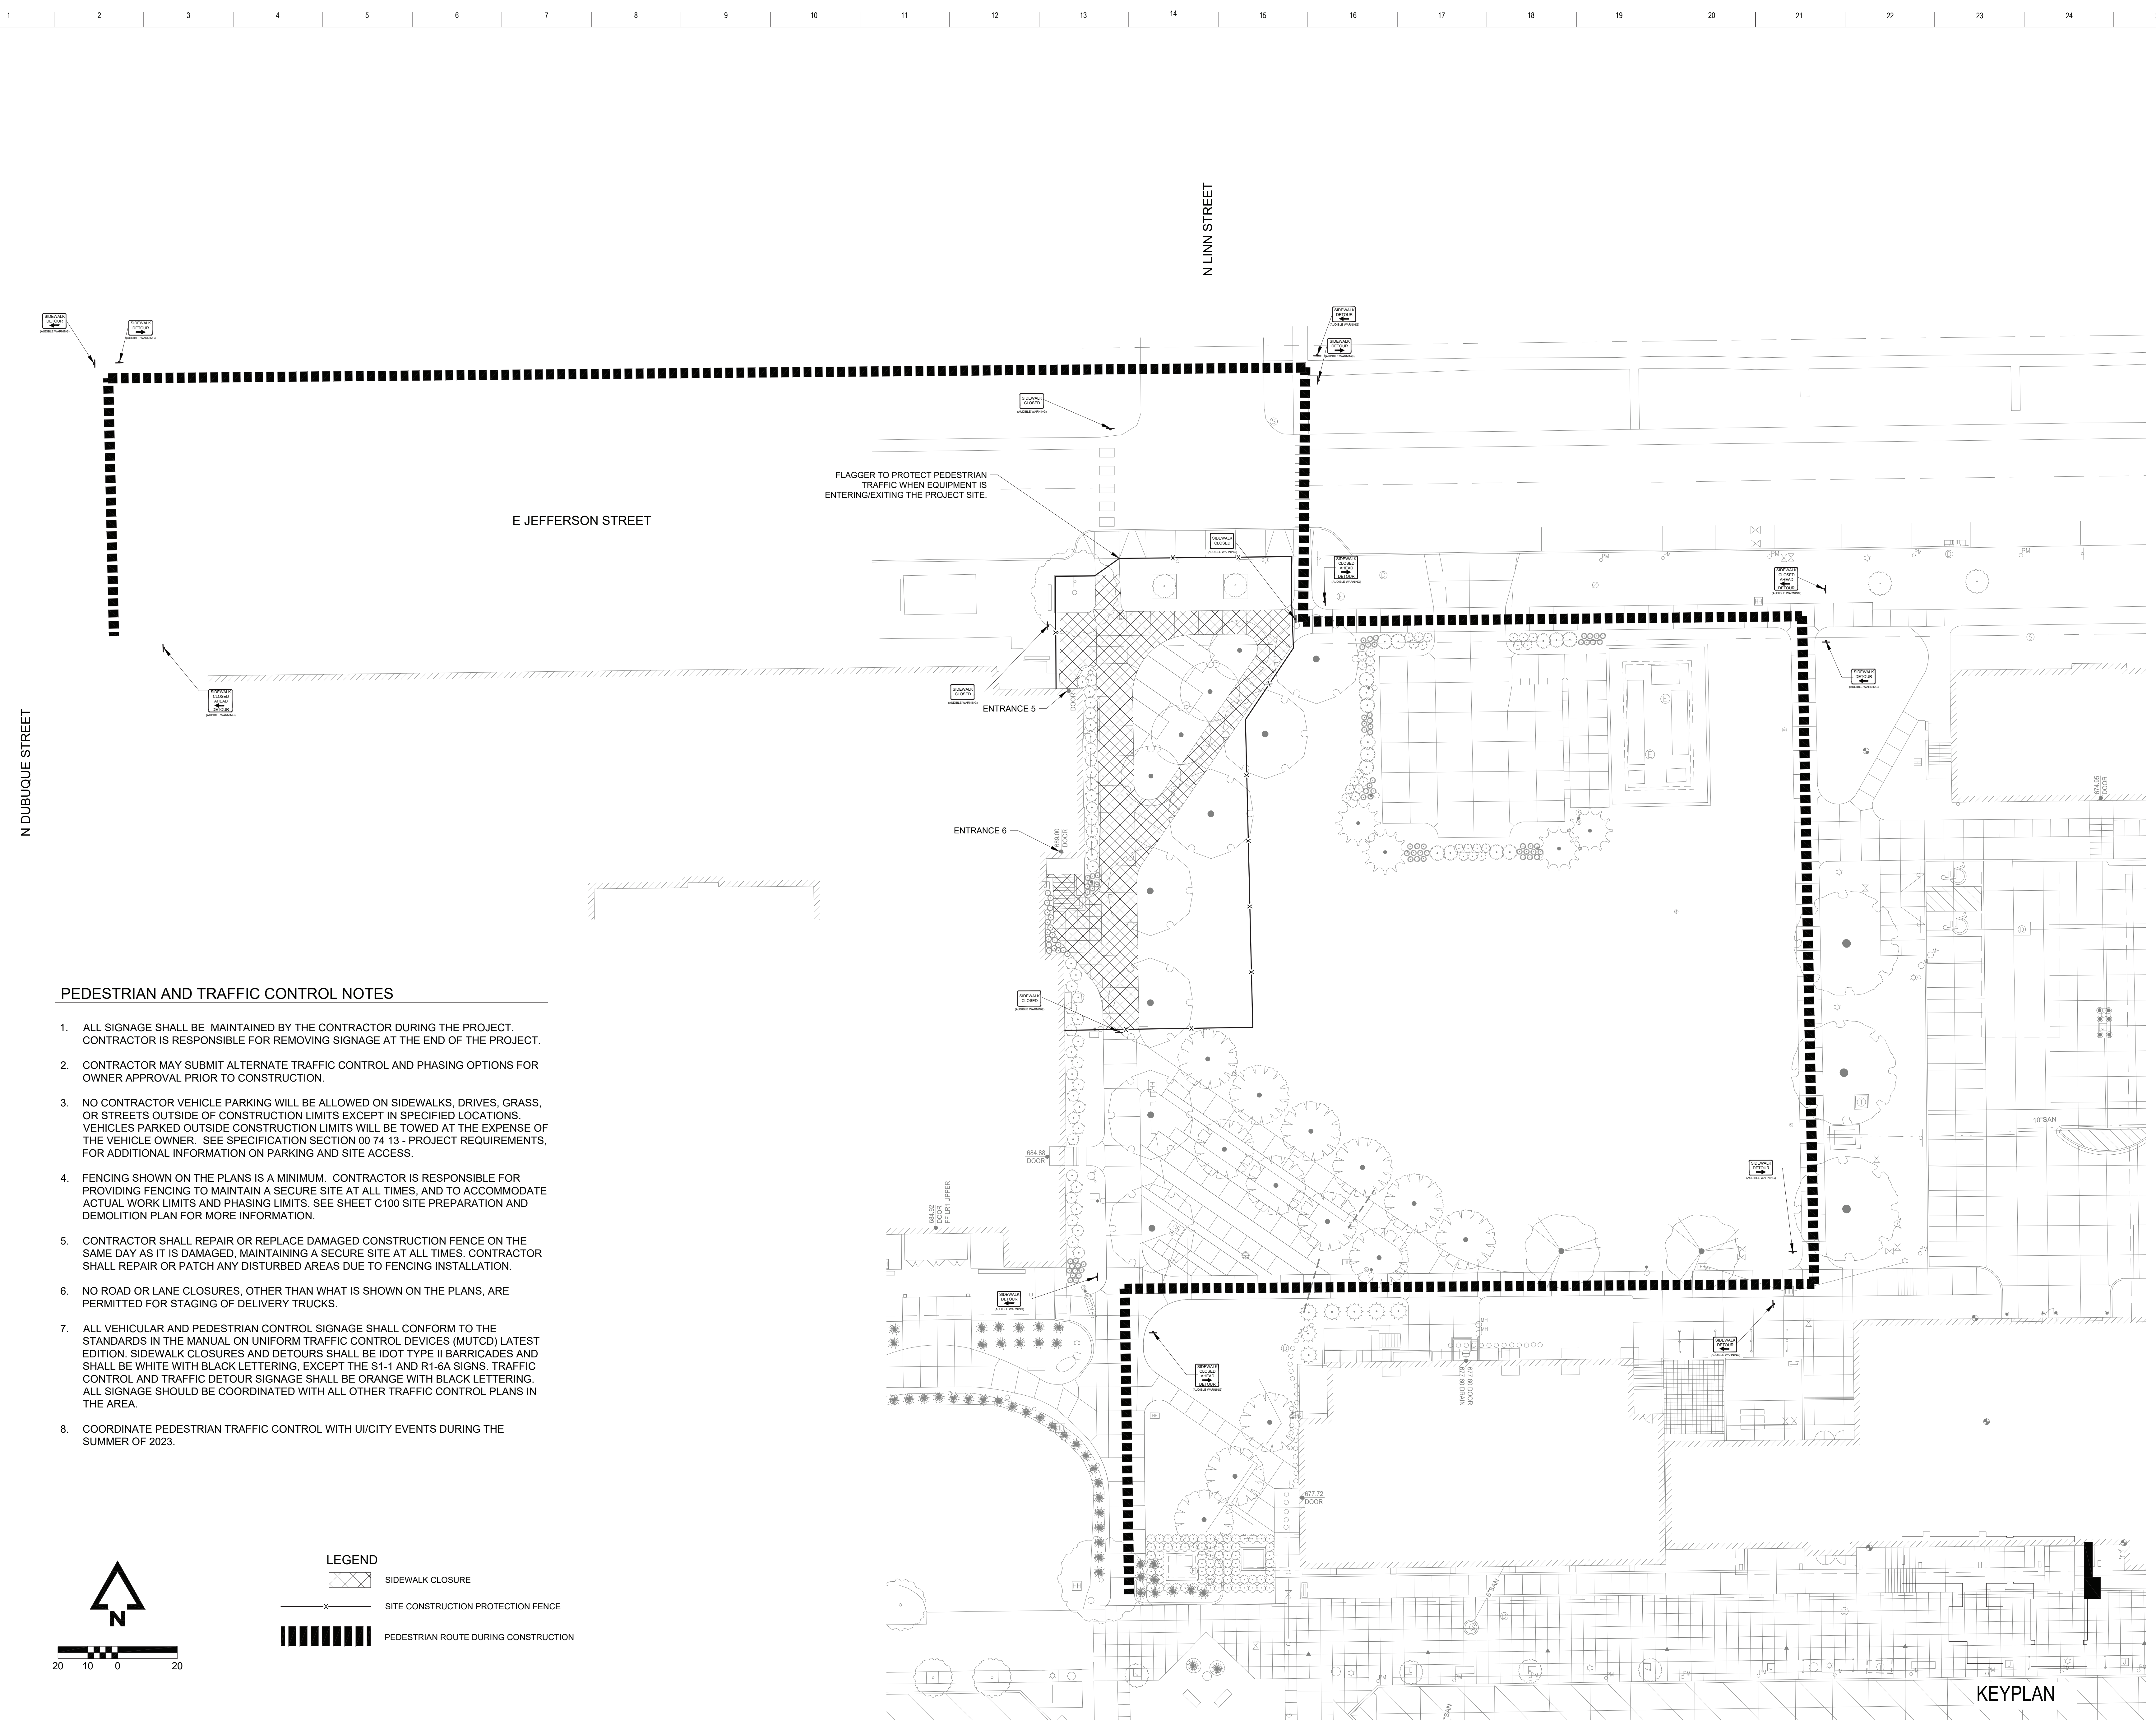

**PEDESTRIAN AND TRAFFIC CONTROL NOTES**

1. ALL SIGNAGE SHALL BE MAINTAINED BY THE CONTRACTOR DURING THE PROJECT. CONTRACTOR IS RESPONSIBLE FOR REMOVING SIGNAGE AT THE END OF THE PROJECT.
2. CONTRACTOR MAY SUBMIT ALTERNATE TRAFFIC CONTROL AND PHASING OPTIONS FOR OWNER APPROVAL PRIOR TO CONSTRUCTION.
3. NO CONTRACTOR VEHICLE PARKING WILL BE ALLOWED ON SIDEWALKS, DRIVES, GRASS, OR STREETS OUTSIDE OF CONSTRUCTION LIMITS EXCEPT IN SPECIFIED LOCATIONS. VEHICLES PARKED OUTSIDE CONSTRUCTION LIMITS WILL BE TOWED AT THE EXPENSE OF THE VEHICLE OWNER. SEE SPECIFICATION SECTION 00 74 13 - PROJECT REQUIREMENTS, FOR ADDITIONAL INFORMATION ON PARKING AND SITE ACCESS.
4. FENCING SHOWN ON THE PLANS IS A MINIMUM. CONTRACTOR IS RESPONSIBLE FOR PROVIDING FENCING TO MAINTAIN A SECURE SITE AT ALL TIMES, AND TO ACCOMMODATE ACTUAL WORK LIMITS AND PHASING LIMITS. SEE SHEET C100 SITE PREPARATION AND DEMOLITION PLAN FOR MORE INFORMATION.
5. CONTRACTOR SHALL REPAIR OR REPLACE DAMAGED CONSTRUCTION FENCE ON THE SAME DAY AS IT IS DAMAGED, MAINTAINING A SECURE SITE AT ALL TIMES. CONTRACTOR SHALL REPAIR OR PATCH ANY DISTURBED AREAS DUE TO FENCING INSTALLATION.
6. NO ROAD OR LANE CLOSURES, OTHER THAN WHAT IS SHOWN ON THE PLANS, ARE PERMITTED FOR STAGING OF DELIVERY TRUCKS.
7. ALL VEHICULAR AND PEDESTRIAN CONTROL SIGNAGE SHALL CONFORM TO THE STANDARDS IN THE MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES (MUTCD) LATEST EDITION. SIDEWALK CLOSURES AND DETOURS SHALL BE IDOT TYPE II BARRICADES AND SHALL BE WHITE WITH BLACK LETTERING, EXCEPT THE S1-11 AND R1-6A SIGNS. TRAFFIC CONTROL AND TRAFFIC DETOUR SIGNAGE SHALL BE ORANGE WITH BLACK LETTERING. ALL SIGNAGE SHOULD BE COORDINATED WITH ALL OTHER TRAFFIC CONTROL PLANS IN THE AREA.
8. COORDINATE PEDESTRIAN TRAFFIC CONTROL WITH UI/CITY EVENTS DURING THE SUMMER OF 2023.

**LEGEND**

- SIDEWALK CLOSURE
- SITE CONSTRUCTION PROTECTION FENCE
- PEDESTRIAN ROUTE DURING CONSTRUCTION

